


Beaver Creek Highway Maintenance Section: Sheet 62 (km 1952 to km 1963)

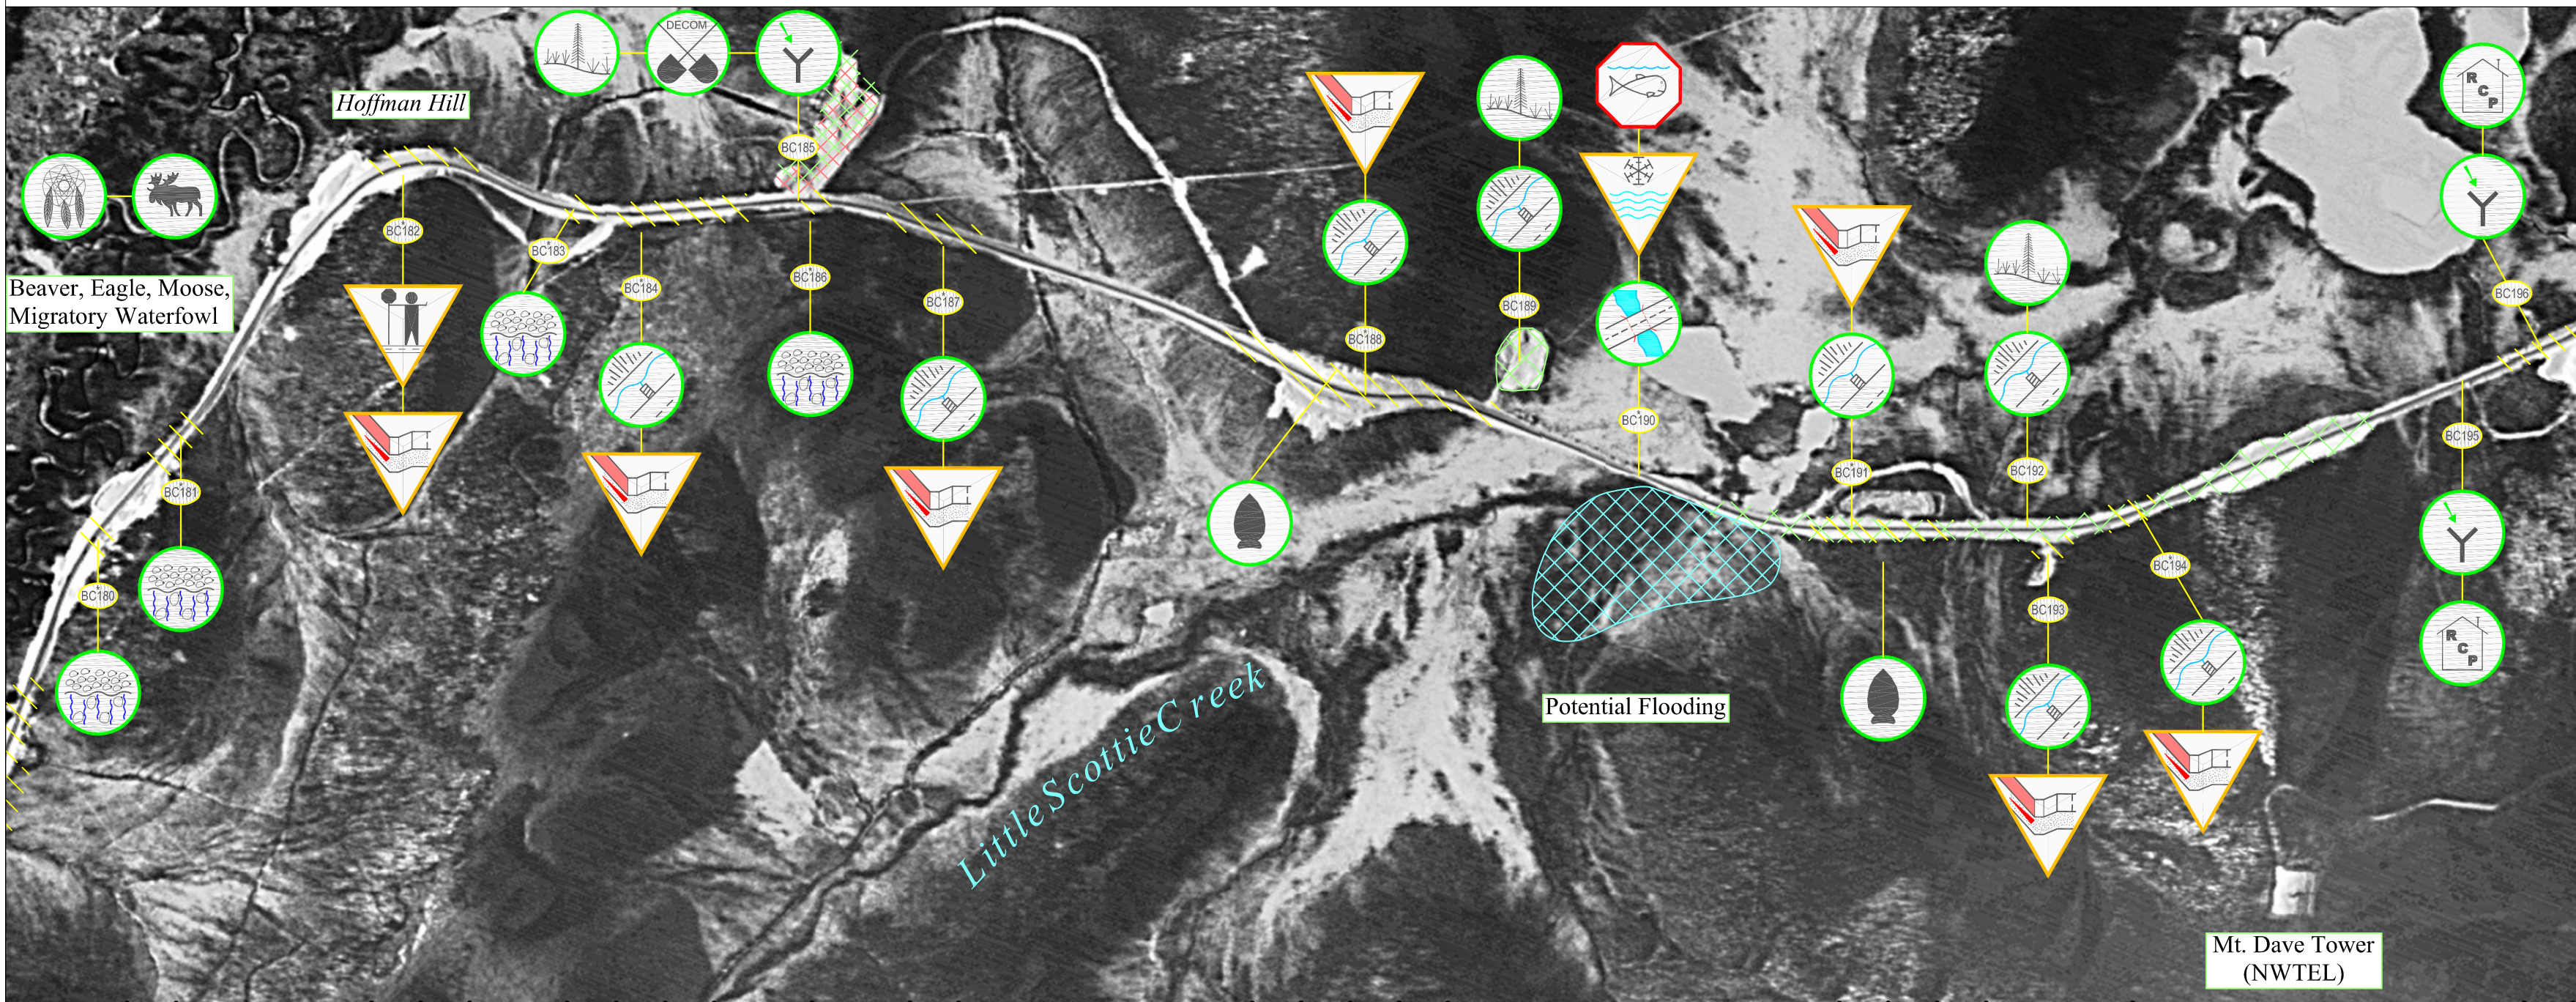

Highway Feature	Engineering Component	Environmental Component	Maintenance Advisory System
<ul style="list-style-type: none"> AC = Access Points BP = Borrow Pits DNG = Drainage (Roadside Ditch, Run-off Control Structures, etc.) Q = Quarries RA = Rest Area RC = Rock Cuts/ Slide Areas PO = Pull Out CV = Culvert MP = Multiplate BR = Bridge UC = Utility encroachment /Crossing IS = Insulated Structure RS = Road Surface GS = Granular Source / Stockpile WX = Wildlife Crossing US = User Safety (eg. Avalanche / Wildlife Area) IC = Icing Control RV = Revegetation (Existing Material, Revegetating & Reclaimed Areas) SF = Snow Fence (drifting control structure) SR = Snow Removal EC = Erosion Control ECP = Erosion Control Protected by Geotextile WM = Waste Management OH = Outhouse GT = Geotextile / Granular Filters CU = Cultural Use HTG = Heritage BL = Boat Launch FH = Fish and/or Fish Habitat RCP = Residential / Commercial Property WQ = Water Quality REC = Recreation WH = Wildlife and/or Wildlife Habitat SV = Scenic Viewing 	<ul style="list-style-type: none"> Mineral Claims 	<ul style="list-style-type: none"> Notification Caution * Alert * <p><small>* Confirm if special maintenance required (Vol. 2., Sec. 1.)</small></p>	<ul style="list-style-type: none"> Soil Remediation Advisory Revegetation Advisory Road Surface Advisory Caution Bar

Notes:
 BC182: Monitor slopes for movement, "km 1955 slide".
 Geotextile under embankment at: BC180, 181, 182, 183, 184, 186, 187, 188, 191, 194.
 BC190: Geotextile under bed, inlet & outlet channels & rip-rap; rock apron in outlet channel.
 BC191: Slope protection both sides.
