


Beaver Creek Highway Maintenance Section: Sheet 63 (km 1961 to km 1965.7 (border))

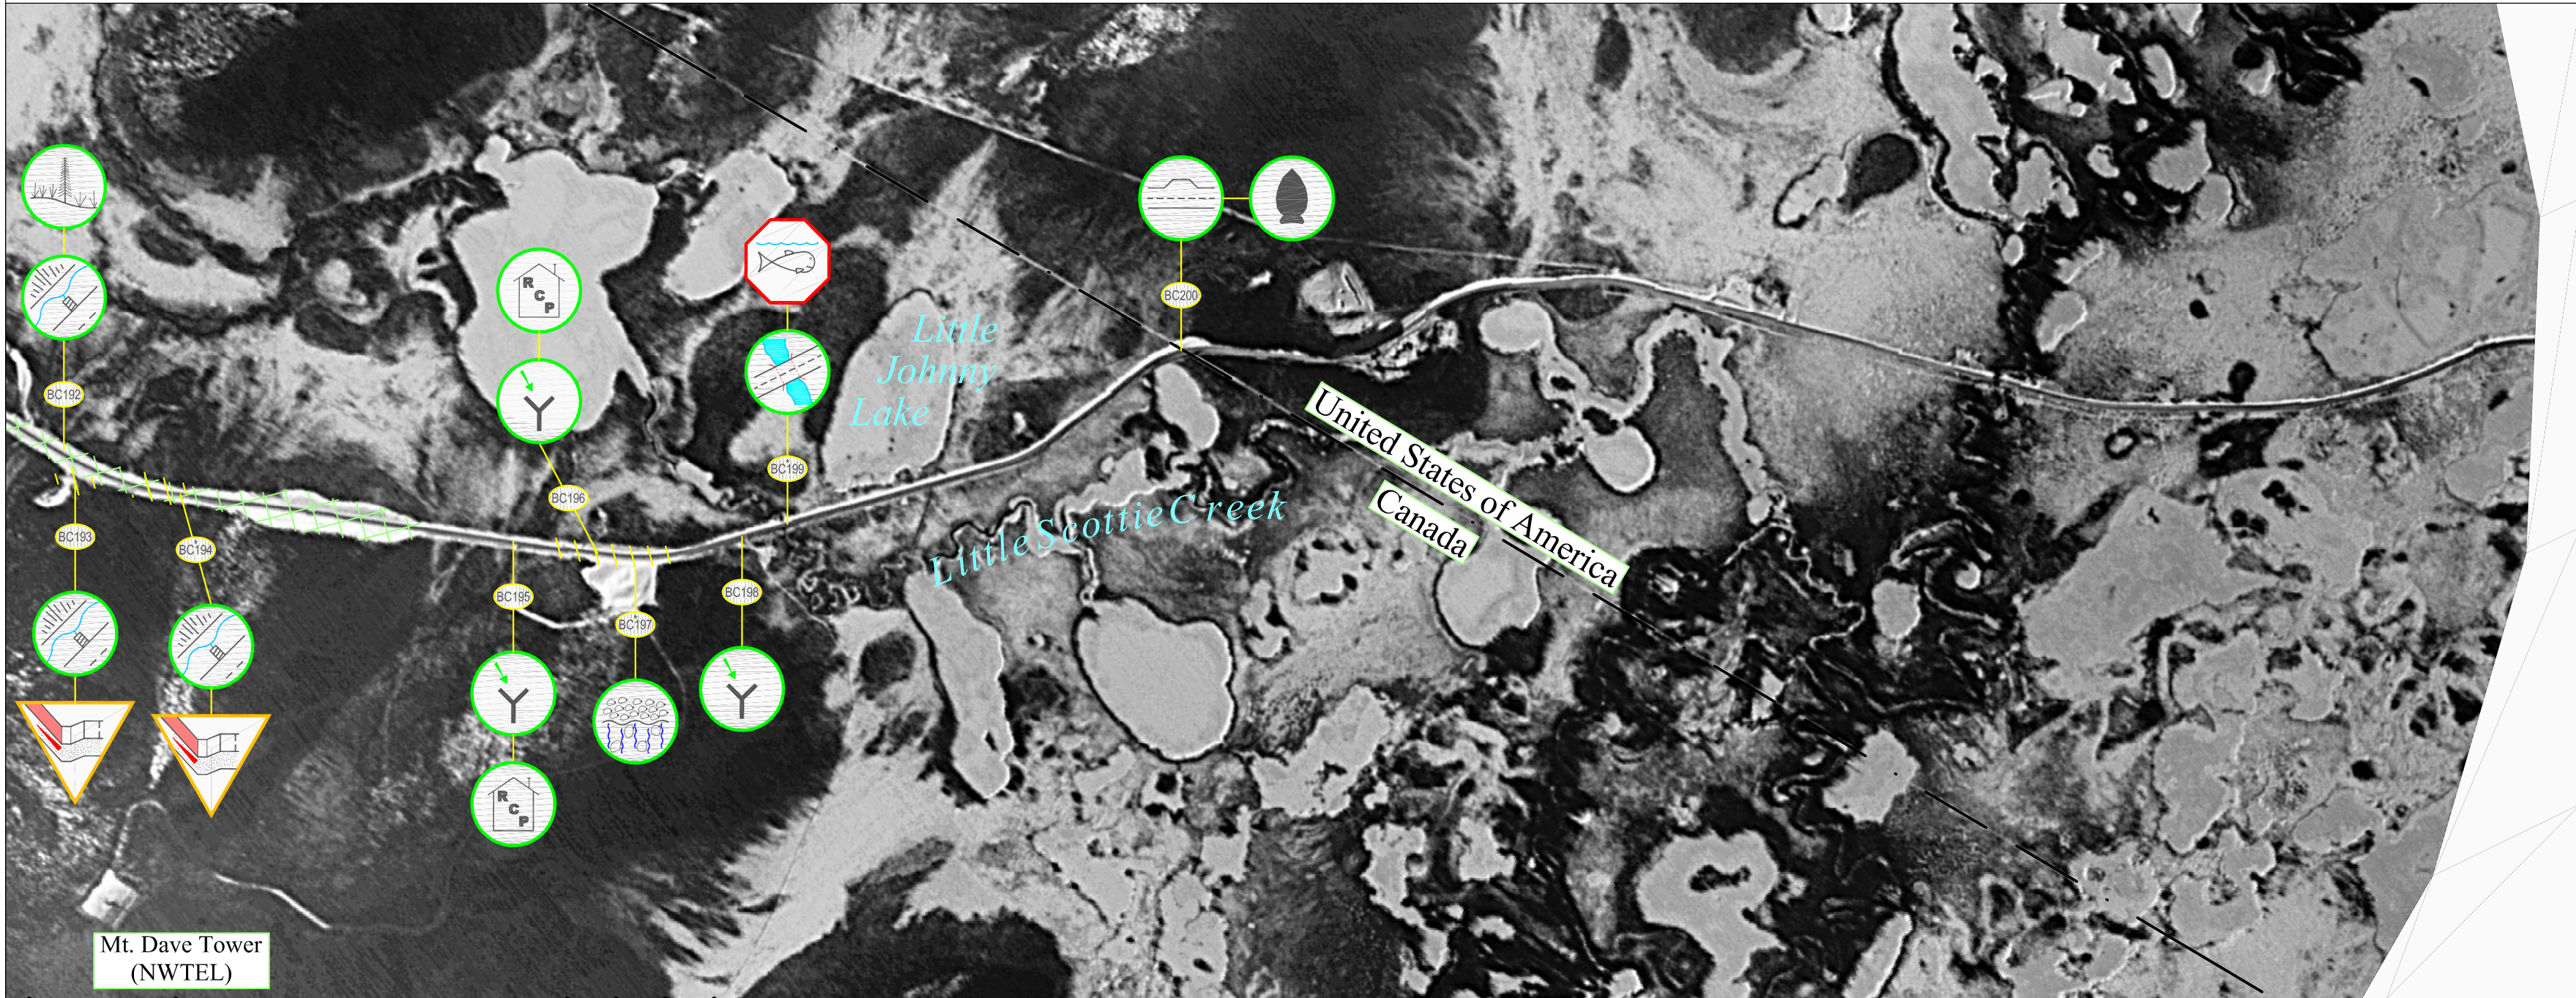

Highway Feature	Engineering Component	Environmental Component	Maintenance Advisory System
<ul style="list-style-type: none"> AC = Access Points BP = Borrow Pits DNG = Drainage (Roadside Ditch, Run-off Control Structures, etc.) Q = Quarries RA = Rest Area RC = Rock Cuts/ Slide Areas PO = Pull Out CV = Culvert MP = Multiplate BR = Bridge UC = Utility encroachment /Crossing IS = Insulated Structure RS = Road Surface GS = Granular Source / Stockpile WX = Wildlife Crossing US = User Safety (eg. Avalanche / Wildlife Area) IC = Icing Control RV = Revegetation (Existing Material, Revegetating & Reclaimed Areas) SF = Snow Fence (drifting control structure) SR = Snow Removal EC = Erosion Control ECP = Erosion Control Protected by Geotextile WM = Waste Management OH = Outhouse GT = Geotextile / Granular Filters CU = Cultural Use HTG = Heritage BL = Boat Launch FH = Fish and/or Fish Habitat RCP = Residential / Commercial Property WQ = Water Quality REC = Recreation WH = Wildlife and/or Wildlife Habitat SV = Scenic Viewing 	<ul style="list-style-type: none"> Notification Caution * Alert * Soil Remediation Advisory Revegetation Advisory Road Surface Advisory Caution Bar 	<ul style="list-style-type: none"> Mineral Claims 	

Notes:
 BC194: Geotextile under embankment.
 BC197: Geotextile under embankment.
 BC199: Geotextile under bed, inlet & outlet channels & rip-rap; rock apron in outlet channel.
